



South Wing Construction Project

JUNE 12, 2019

Message from the VPAA -

Here is the second newsletter on the South Wing construction update. I have included projected deadlines and completion updates for various aspects of the project, a plan-view of the desk/pod layout and 3-D renderings of the completed Great Hall renovation. Again, if there is a particular aspect of the project about which you would like to hear, let me know (vpaa@neomed.edu) and I will try to provide the information in future newsletters.

Richard Kasmer-


Projected Timelines and Completion Rates for Phase I –

Provided below is an abbreviated list of tasks and timelines for this project. As always, any construction project may have delivery problems, construction delays or other unpredictable events that may alter this timeline. In case this project has not proceeded in a timely fashion, a “Plan B” has already been created and is in place that will allow all classroom activities to be completed for the **entire** Fall 2019 semester in alternate locations (Ballroom, Cooke Alumni Hall, MDL, etc.). An assessment of room readiness will be made by the faculty on the Construction Team on September 13, 2019 and this information would be shared broadly with all faculty, students and staff. This is noted as the Academic Decision in the timeline below.

Project Tasks*	Projected End-Date	Percent Complete
Demolition of Great Hall & Training Room	May 10, 2019	100%
Furniture decisions	May 17, 2019	100%
Lighting, wallcovering & carpet color decisions	June 5, 2019	25%
Electric floor boxes & painting	July 22, 2019	0%
Cabling for wireless upgrade	July 26, 2019	45%
Ceiling lighting & carpeting	July 29, 2019	0%
Build and test first desk/pod for Great Hall	August 5, 2019	0%
Wireless and Network upgrade	August 15, 2019	5%
Academic Decision on room readiness	September 13, 2019	0%
Configure remaining 29 desks/pods for Great Hall	September 17, 2019	0%
Final testing and faculty training for Great Hall	September 20, 2019	0%
Final preparations for Great Hall to ‘go live’	October 9, 2019	0%

*Data provided by Geri Hein, Project Mgr., Office of Information Technology

Great Hall - Plan-view of 30 desk/pod configuration –

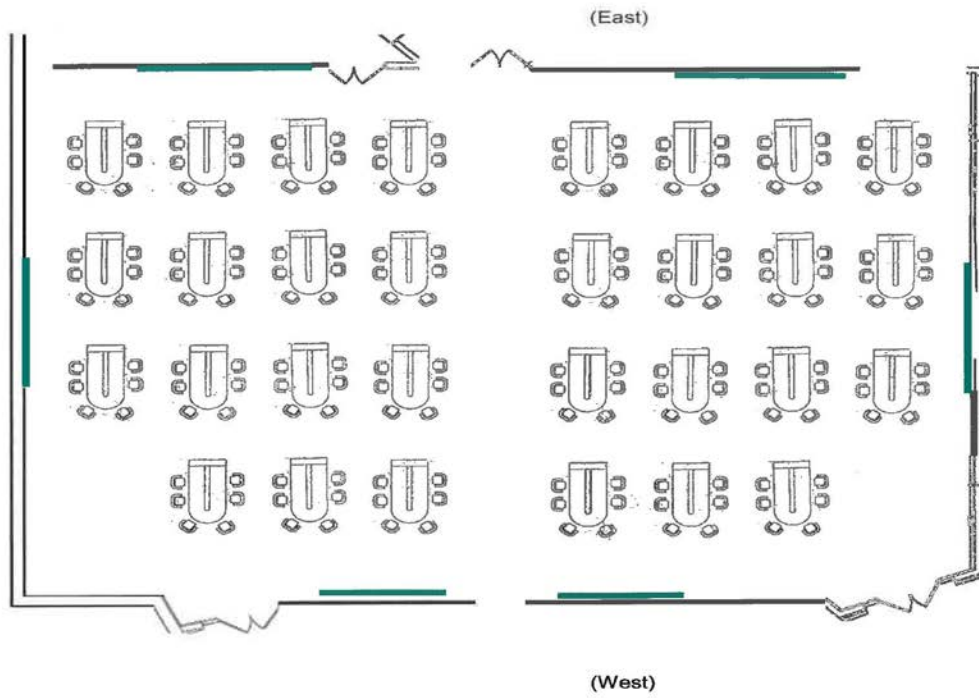

Great Hall – Rendering of Completed Renovation –



Great Hall – Renderings of Desks/Pods with Monitors in the Up position –

